ID	Task Name	Duration	Start	Finish
1	**ELECTRICAL FITOUT PROGRAM**	**50 days**	**Mon 28/08/06**	**Fri 03/11/06**
2	**Owners Trainers Ground Floor**	**35 days**	**Mon 28/08/06**	**Fri 13/10/06**
3	First Fix General	15 days	Mon 28/08/06	Fri 15/09/06
4	Building Weather Tight and dry	0 days	Fri 15/09/06	Fri 15/09/06
5	Second Fix GS	10 days	Mon 18/09/06	Fri 29/09/06
6	Second Fix Lights	10 days	Mon 18/09/06	Fri 29/09/06
7	Ceilings and Decoration	0 days	Fri 29/09/06	Fri 29/09/06
8	Second Fix Intruder / cctv	5 days	Mon 02/10/06	Fri 06/10/06
9	Second Fix Fire Alarm	5 days	Mon 02/10/06	Fri 06/10/06
10	Second Fix Mechanical Plant	5 days	Mon 02/10/06	Fri 06/10/06
11	Second Fix Data	5 days	Mon 02/10/06	Fri 06/10/06
12	Third Fix and Comissioning	5 days	Mon 09/10/06	Fri 13/10/06
13	**Owners Trainers First Floor**	**30 days**	**Mon 25/09/06**	**Fri 03/11/06**
14	First Fix General	10 days	Mon 25/09/06	Fri 06/10/06
15	Building Weather Tight and dry	0 days	Fri 06/10/06	Fri 06/10/06
16	Second Fix GS	10 days	Mon 09/10/06	Fri 20/10/06
17	Second Fix Lights	10 days	Mon 09/10/06	Fri 20/10/06
18	Ceilings and Decoration	0 days	Fri 20/10/06	Fri 20/10/06
19	Second Fix Intruder / cctv	5 days	Mon 23/10/06	Fri 27/10/06
20	Second Fix Fire Alarm	5 days	Mon 23/10/06	Fri 27/10/06
21	Second Fix Mechanical Plant	5 days	Mon 23/10/06	Fri 27/10/06
22	Second Fix Data	5 days	Mon 23/10/06	Fri 27/10/06
23	Third Fix and Comissioning	5 days	Mon 30/10/06	Fri 03/11/06
24	**Stable Block Installation**	**25 days**	**Mon 18/09/06**	**Fri 20/10/06**
25	Completion of Stables 54-84 & 1-30 85-118 Inclusive	0 days	Mon 18/09/06	Mon 18/09/06
26	First Fix Containment	5 days	Mon 18/09/06	Fri 22/09/06
27	Second Fix GS	10 days	Mon 25/09/06	Fri 06/10/06
28	Second Fix Lights	10 days	Mon 25/09/06	Fri 06/10/06
29	Second Fix Intruder / cctv	5 days	Mon 09/10/06	Fri 13/10/06
30	Second Fix Fire Alarm	5 days	Mon 09/10/06	Fri 13/10/06
31	Third Fix and Comissioning	5 days	Mon 16/10/06	Fri 20/10/06
32	**Mains Power Installation**	**16 days**	**Wed 13/09/06**	**Wed 04/10/06**
33	Ducting Complete	0 days	Wed 13/09/06	Wed 13/09/06
34	Measure and order Cables	5 days	Wed 13/09/06	Tue 19/09/06
35	Install Cables	4 days	Wed 20/09/06	Mon 25/09/06
36	Install Boards	2 days	Wed 20/09/06	Thu 21/09/06
37	Terminate Cables	5 days	Tue 26/09/06	Mon 02/10/06
38	Third Fix and Comissioning	2 days	Tue 03/10/06	Wed 04/10/06
39	**Communication Installation**	**16 days**	**Wed 13/09/06**	**Wed 04/10/06**
40	Ducting Complete	0 days	Wed 13/09/06	Wed 13/09/06
41	Measure and order Cables	5 days	Wed 13/09/06	Tue 19/09/06
42	Install Cables	4 days	Wed 20/09/06	Mon 25/09/06
43	Install Krone Boxes	2 days	Wed 20/09/06	Thu 21/09/06
44	Terminate Cables	5 days	Tue 26/09/06	Mon 02/10/06
45	Third Fix and Comissioning	2 days	Tue 03/10/06	Wed 04/10/06

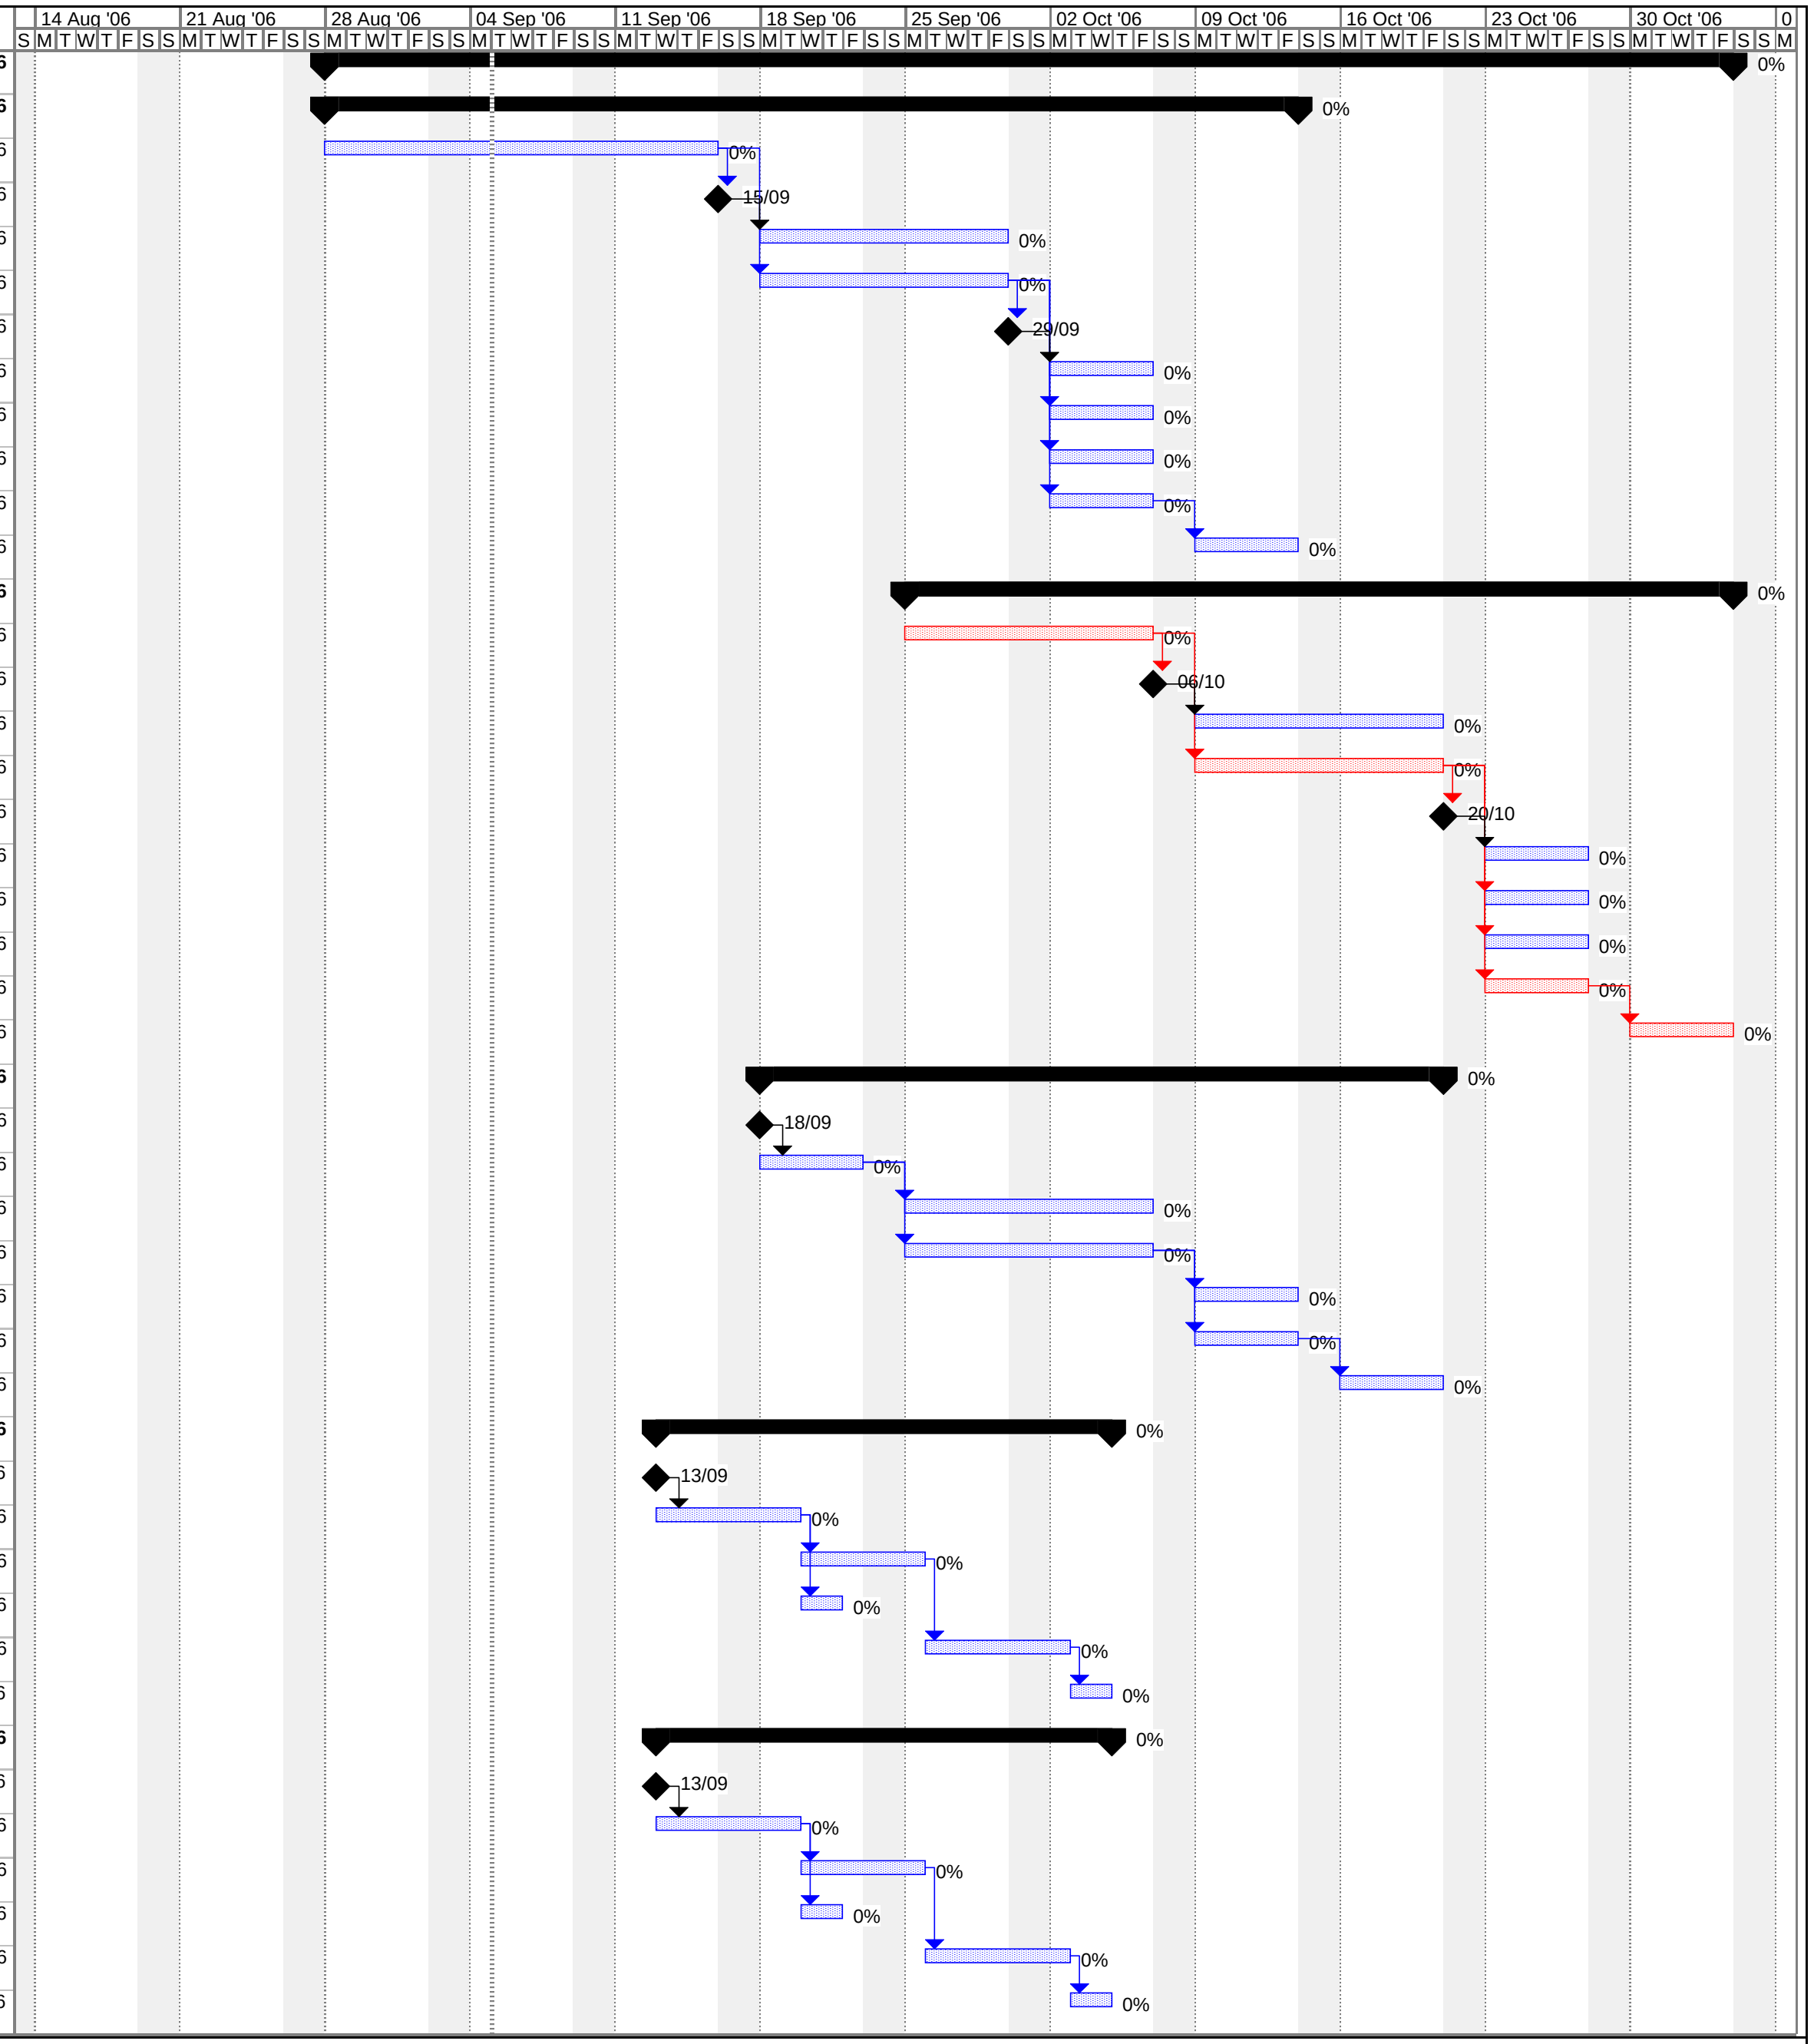

Project: Electrical 020906 m98
Date: Tue 05/09/06

Critical | Task | Baseline | Milestone | Project Summary | External Milestone
Critical Split | Split | Baseline Split | Summary Progress | External Tasks | Deadline
Critical Progress | Task Progress | Baseline Milestone | Summary | External Milestone
